



# **Rouge Valley Trail Project Update**

## **Presentation to Development Services Committee**

### **Engineering Department November 8, 2021**




## Agenda

- Completed Trail Sections to date
- Proposed Directional and Regulatory Signage for the trail
  - as per November 6, 2020 Budget Committee Meeting
- Remaining Works and Schedule
- Recommendations



# Completed Trail Sections to date

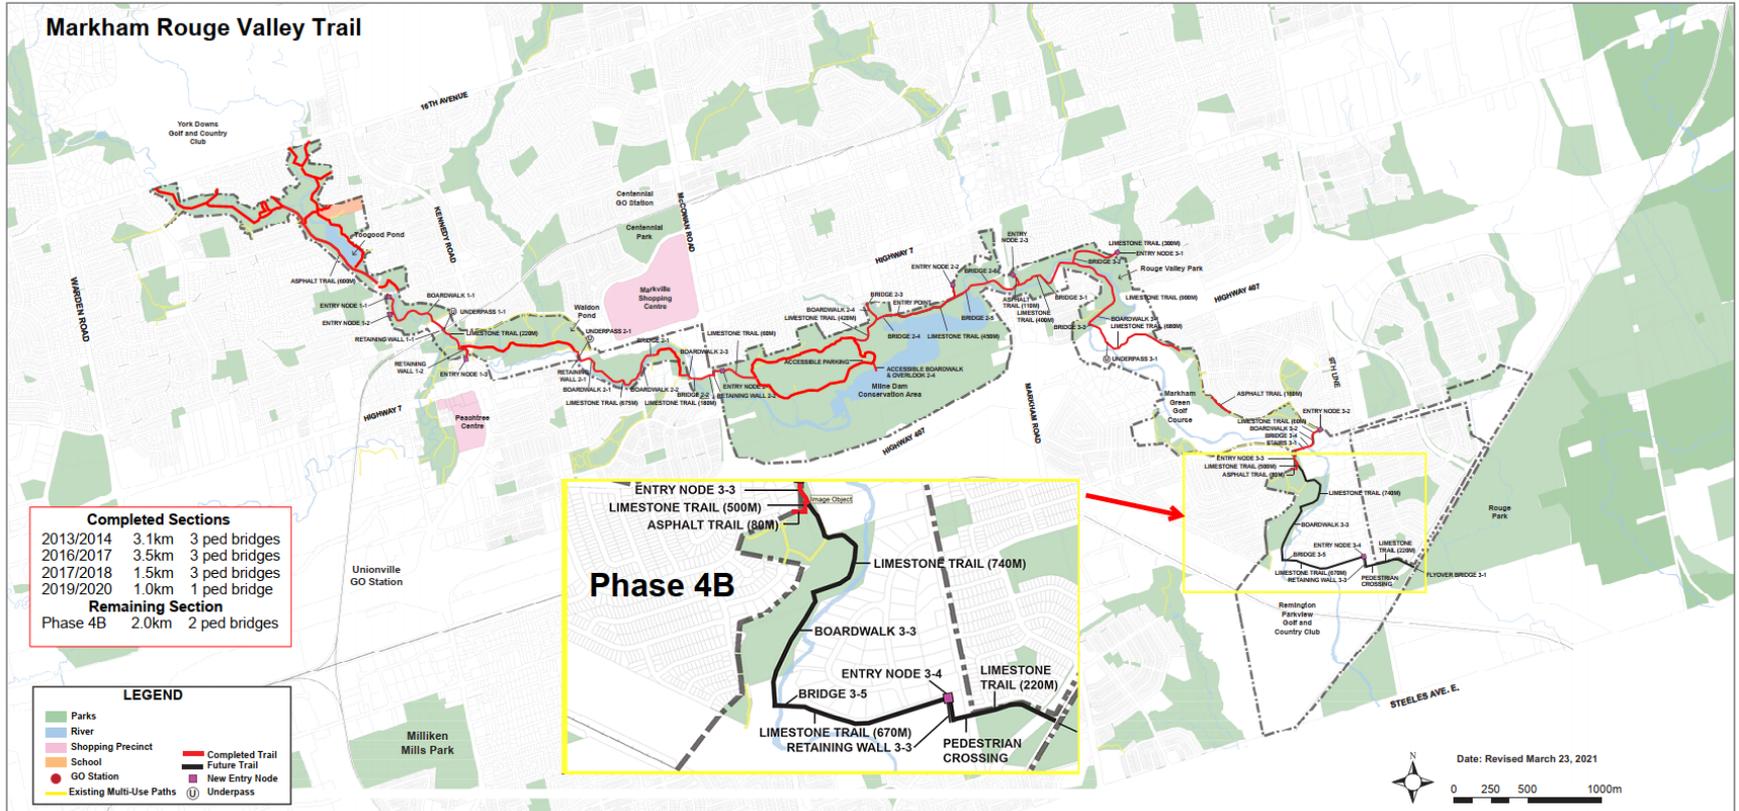




## Completed Trail Sections to date – cont'd

- Rouge Valley Trail Highlights (16<sup>th</sup> Avenue to 14<sup>th</sup> Avenue):
  - Construction commenced in 2013, and completed in 2020
  - Total length of trails completed – ±11.0km
  - Total length of boardwalks constructed – ±500m
  - Entry Nodes constructed - 11
  - Pedestrian bridges constructed – 10







# Rouge Valley Trail Direction and Regulatory Proposed Signage





# Rouge Valley Trail – Way Finding Signs (Options under consideration)

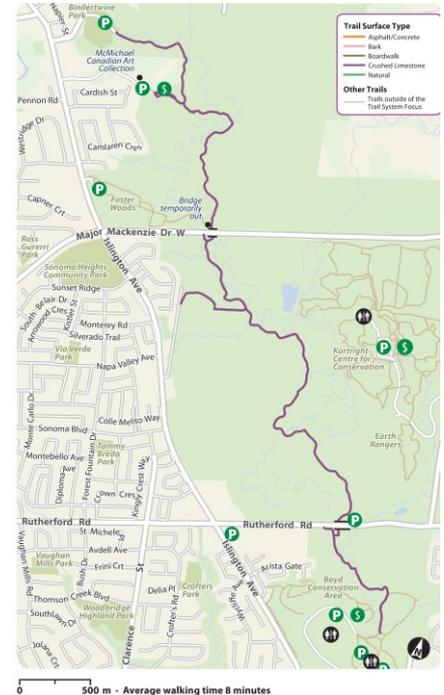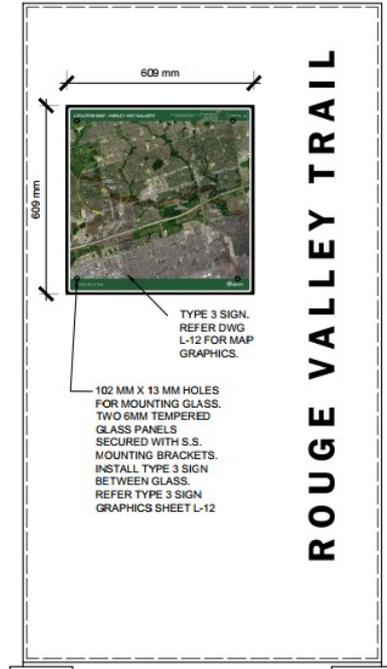





# Rouge Valley Trail – Remaining Works


## Phase 4B - 14<sup>th</sup> Avenue to DCP

- Design – 2022
- Property Acquisition / Permits – 2023
- Construction – 2024 (Tentative)
- Total length of Trail - ±2.0km
- Pedestrian Bridges - 2

## DCP Crossing - TBD

## Denison Road Extension EA

- EA has commenced
- Design – 2022 / 2023
- Construction – TBD

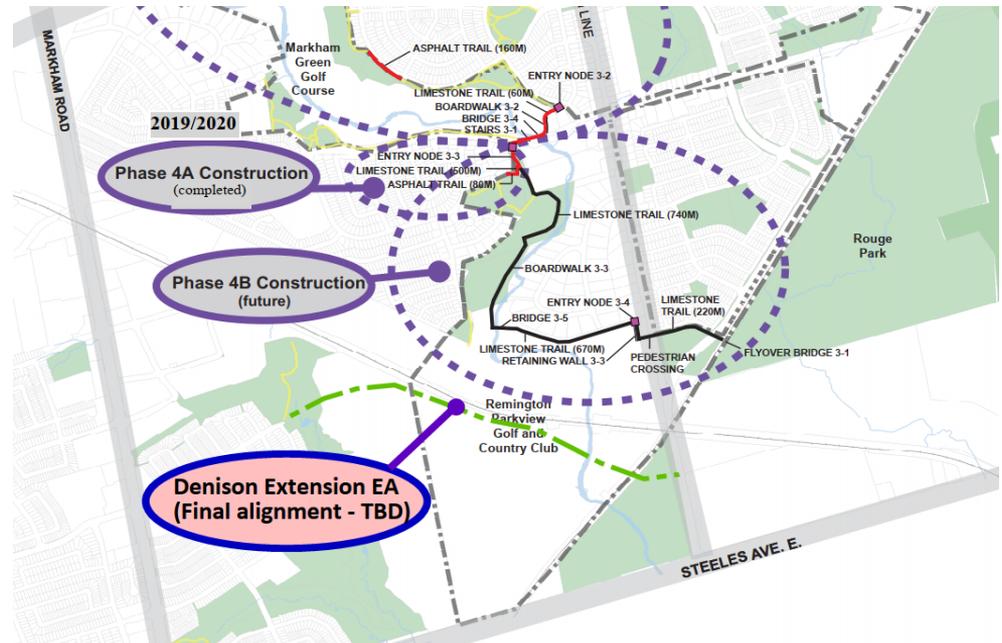





## DSC Recommendations

- Staff be authorized to issue the tender for the installation of the directional and regulatory signs for the Rouge Valley Trail
- Staff continue to work on the options for the Wayfinding systems and Interpretive signs for the Rouge Valley Trail System and report back to DSC
